



Project: Facilities_6_03 Date: 1/15/04	Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
	Progress		Summary		Rolled Up Milestone		Split		Project Summary			

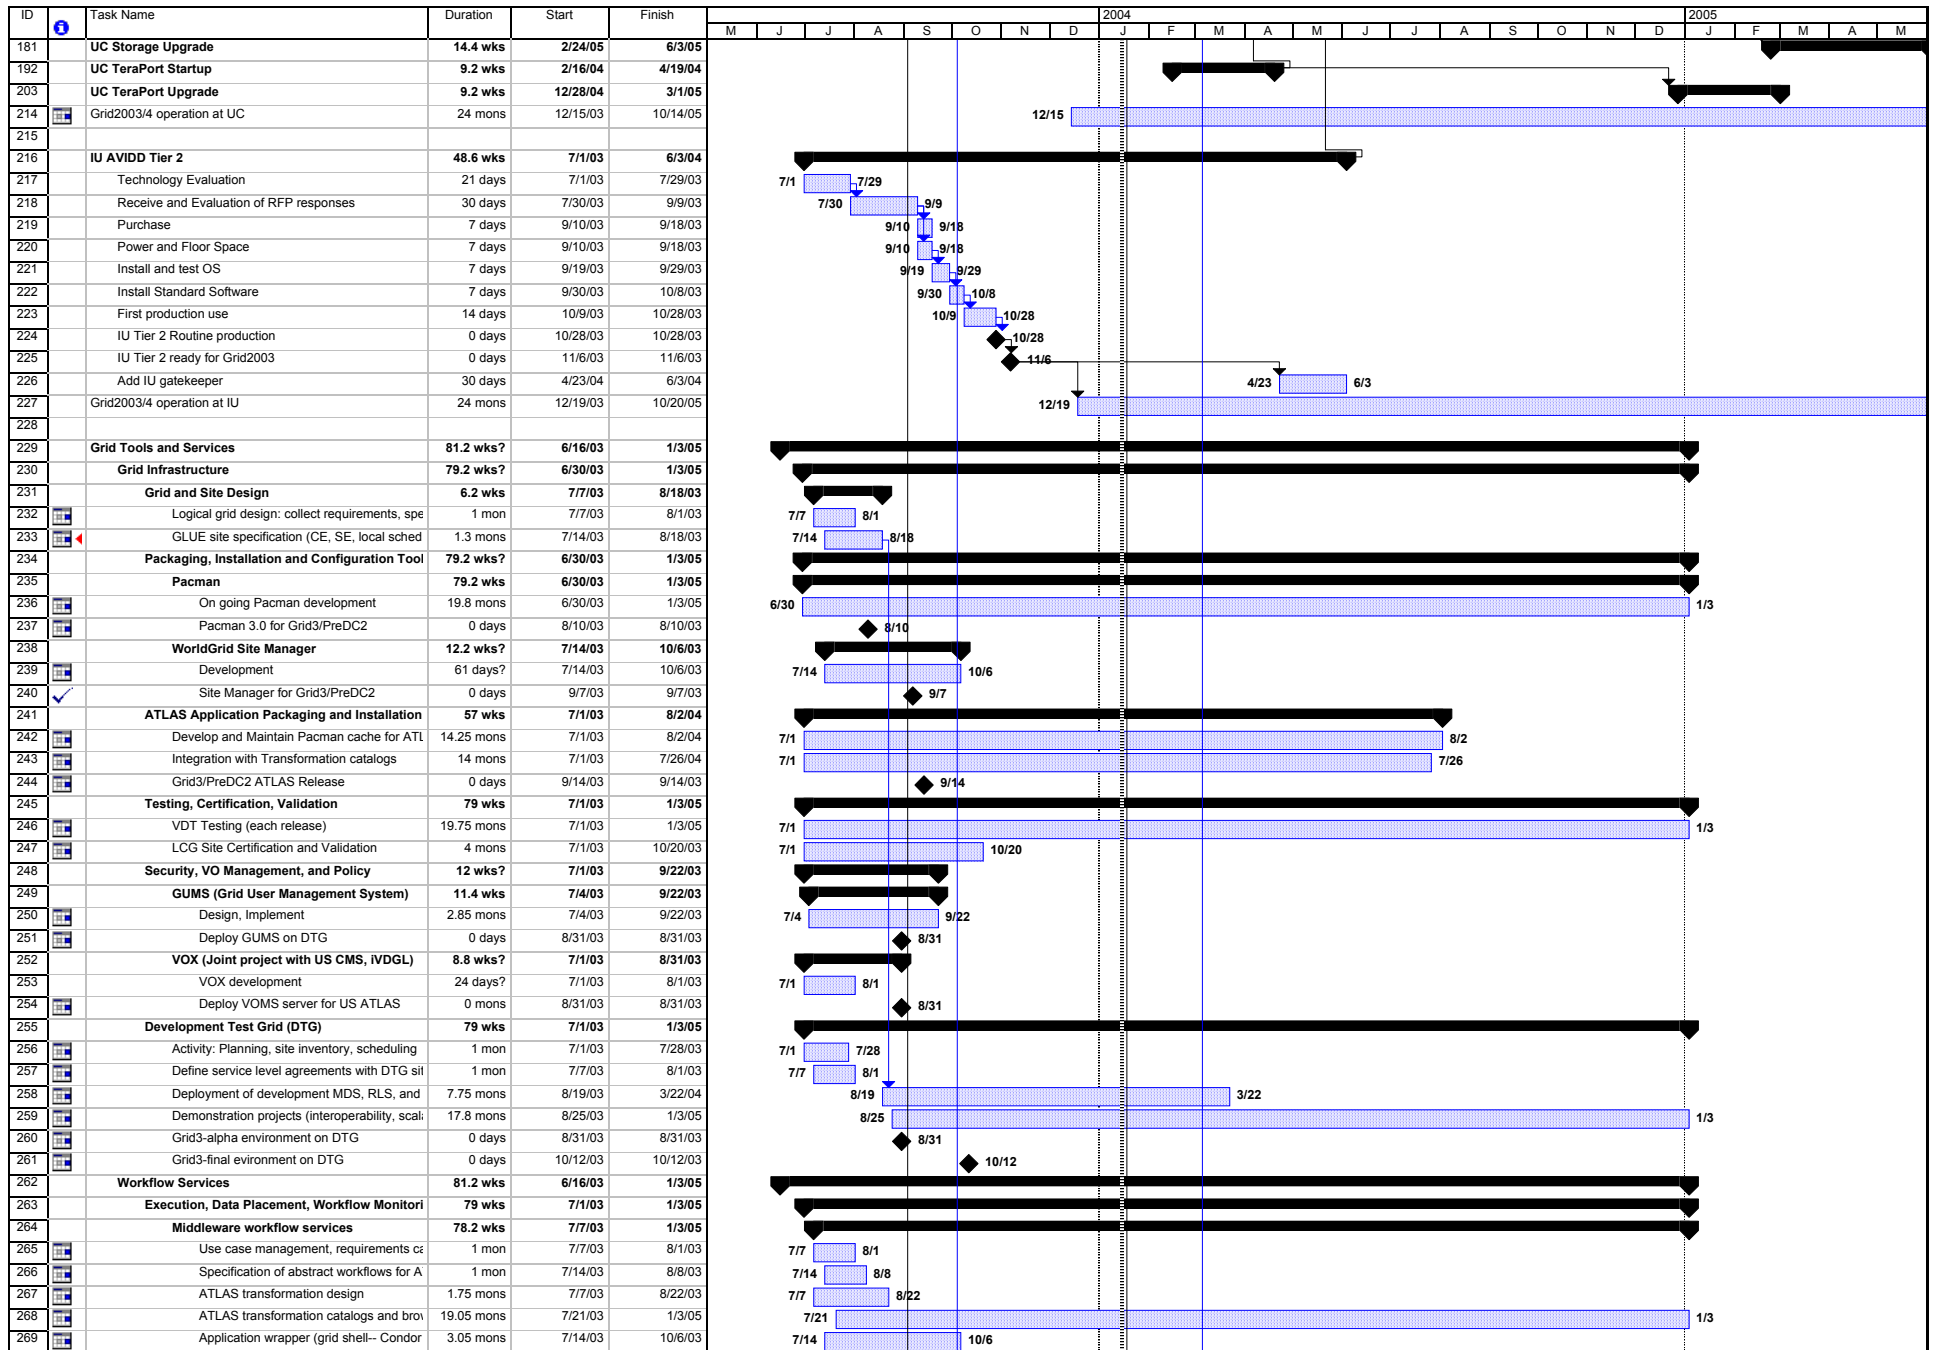

Project: Facilities_6_03
Date: 1/15/04

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

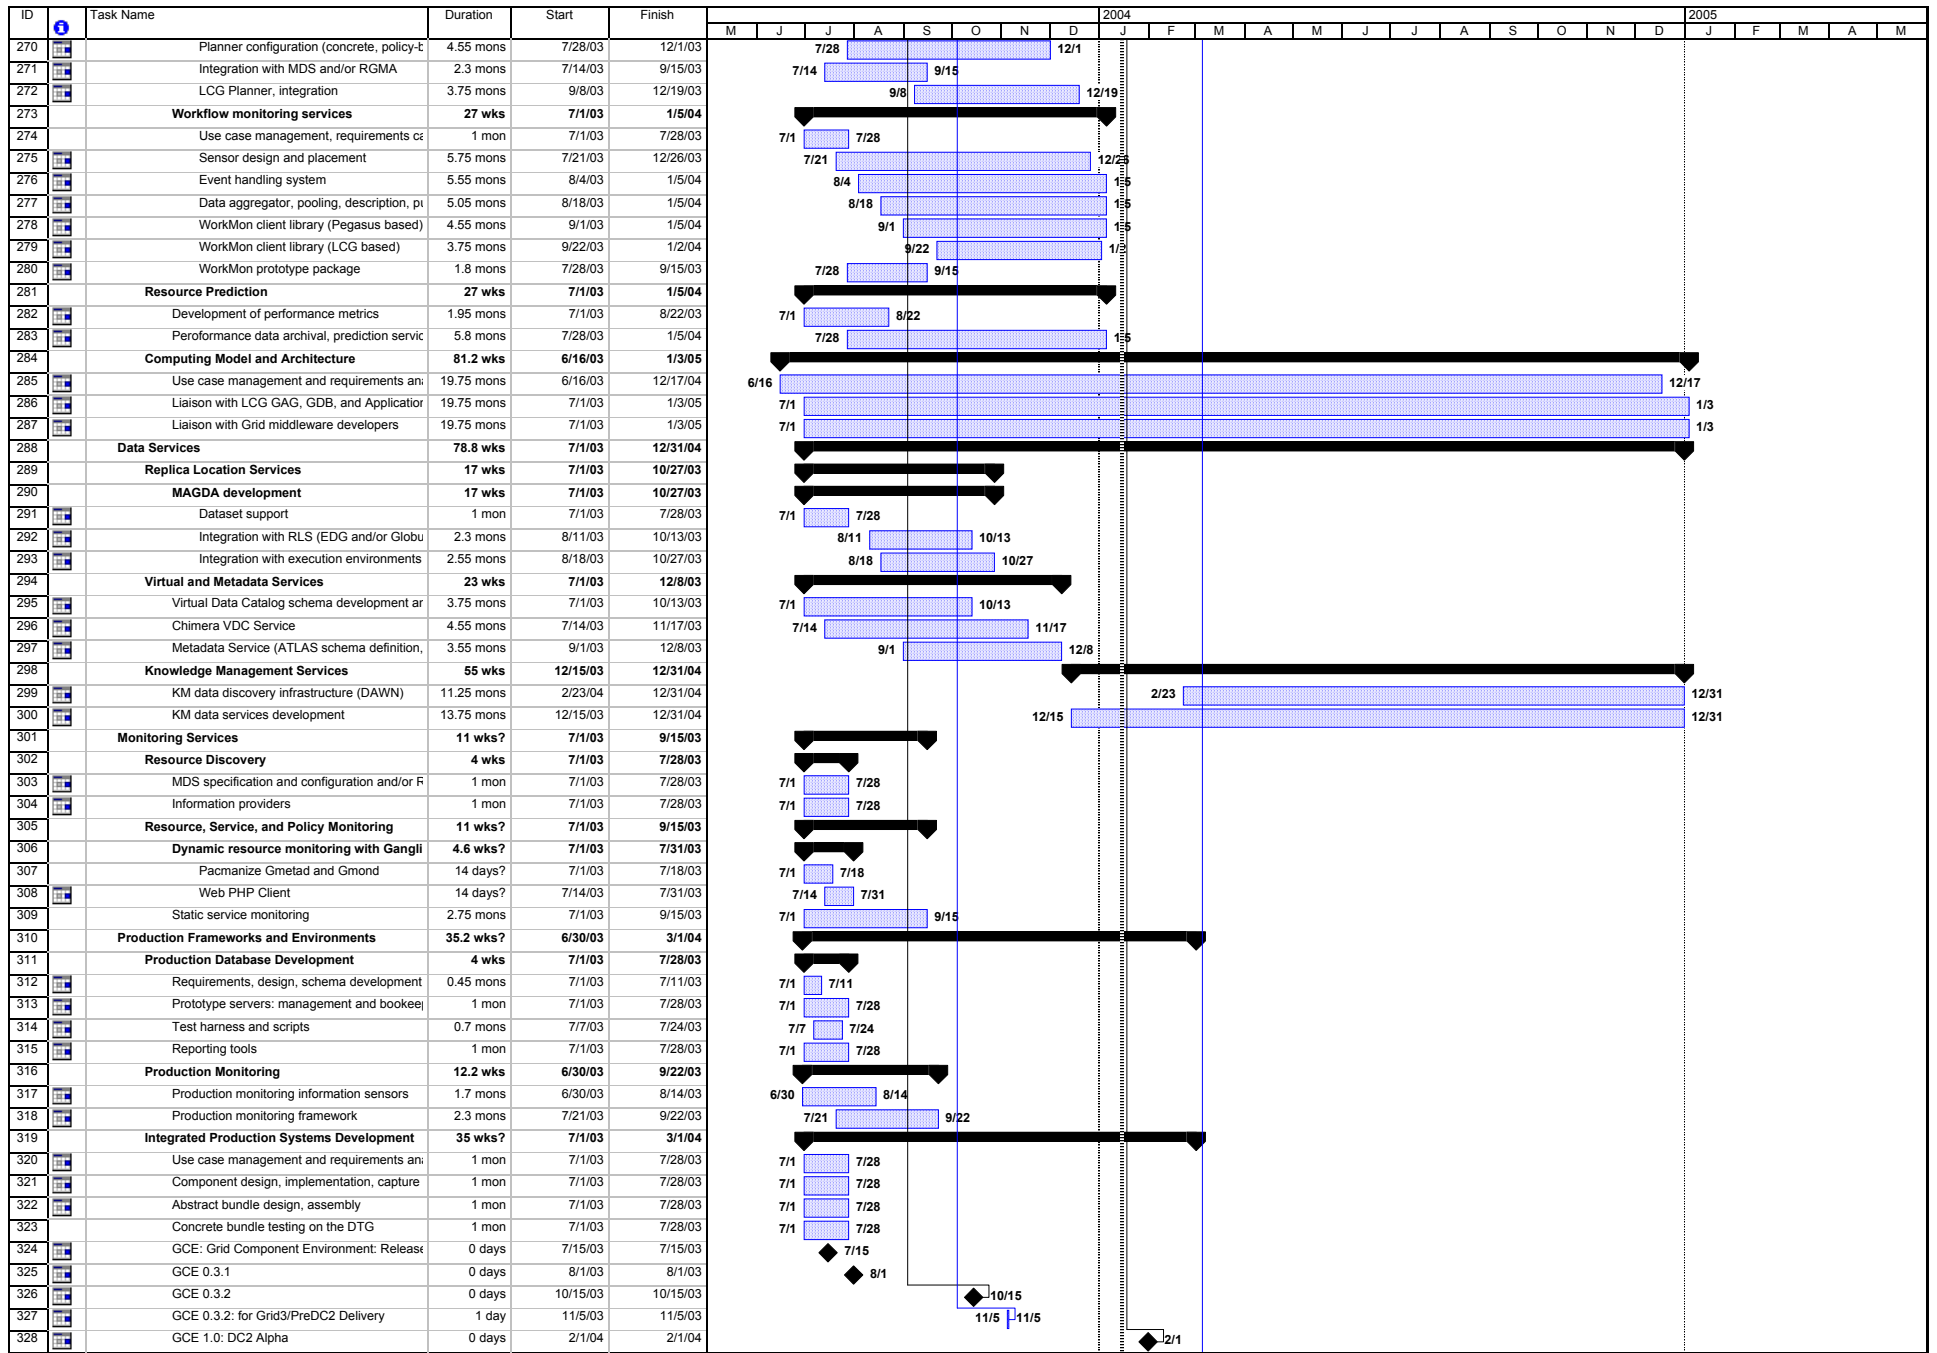

Project: Facilities_6_03
 Date: 1/15/04

Task: Milestone:
 Progress: Summary:

Rolled Up Task: Rolled Up Progress:
 Rolled Up Milestone: Split:

External Tasks: Group By Summary:
 Project Summary:

ID	Task Name	Duration	Start	Finish	2004												2005																															
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M																			
329	GCE 1.0: DC2 Delivery	1 day?	3/1/04	3/1/04													J	F	M	A	M	J	J	A	S	O	N	D																				
330	Production User Tools and Services	30.2 wks	6/30/03	1/26/04	[Task Bar]																																											
331	Command line toolsets	4 mons	6/30/03	10/17/03	6/30 10/17																																											
332	Web portal integration	7.5 mons	7/1/03	1/26/04	7/1 1/26																																											
333	Analysis Frameworks	79 wks	7/1/03	1/3/05	[Task Bar]																																											
334	Distributed Interactive Analysis	79 wks	7/1/03	1/3/05	[Task Bar]																																											
335	DIAL (Distributed Interactive Analysis of Larg	19.75 mons	7/1/03	1/3/05	7/1 1/3																																											
336	GANGA (Python-based Athena Grid Interfac	19.75 mons	7/1/03	1/3/05	7/1 1/3																																											
337	Grid Portlet Framework (Grappa)	3.25 mons	7/1/03	9/29/03	7/1 9/29																																											
338	Advanced Analysis Environments	70 wks	9/1/03	12/31/04	[Task Bar]																																											
339	Dynamic Workspaces (DAWN toolkit, protoco	17.5 mons	9/1/03	12/31/04	9/1 12/31																																											
340	Collaborative Grid Environments, CHEF base	17.5 mons	9/1/03	12/31/04	9/1 12/31																																											
341																																																
342																																																
343	LCG-3 Full Service Available	0 wks	1/28/05	1/28/05	◆ 1/28																																											
344	Permanent Tier 2 Sites C & D selection complete	0 wks	5/2/05	5/2/05																																												
345	Tier 1 Fabric upgrade fully operational for DC3	0 wks	7/1/05	7/1/05																																												
346	Start ATLAS DC3	0 wks	7/1/05	7/1/05																																												
347	LCG Computing TDR	0 wks	7/1/05	7/1/05																																												
348	Tier 1 Fabric upgrade fully operational for DC4	0 wks	11/1/05	11/1/05																																												
349	Start ATLAS DC4	0 wks	11/1/05	11/1/05																																												
350	Computing MOU signed	0 wks	1/2/06	1/2/06																																												
351	Permanent Tier 2 Sites E selection complete	0 wks	1/16/06	1/16/06																																												
352	Tier 1 Fabric full operation at 15% capacity	0 wks	10/2/06	10/2/06																																												
353	Start Full Chain Test in Real Environment	0 wks	10/2/06	10/2/06																																												
354	Tier 1 Fabric full operation at 30% capacity	0 wks	5/1/07	5/1/07																																												
355	LHC Startup	0 wks	5/1/07	5/1/07																																												
356	Tier 1 Fabric full operation at 100% capacity	0 wks	7/1/08	7/1/08																																												
357	100% Capacity for LHC	0 wks	7/1/08	7/1/08																																												


Project: Facilities_6_03
Date: 1/15/04

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			


2006												2007												2008														
J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A

Project: Facilities_6_03
Date: 1/15/04

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

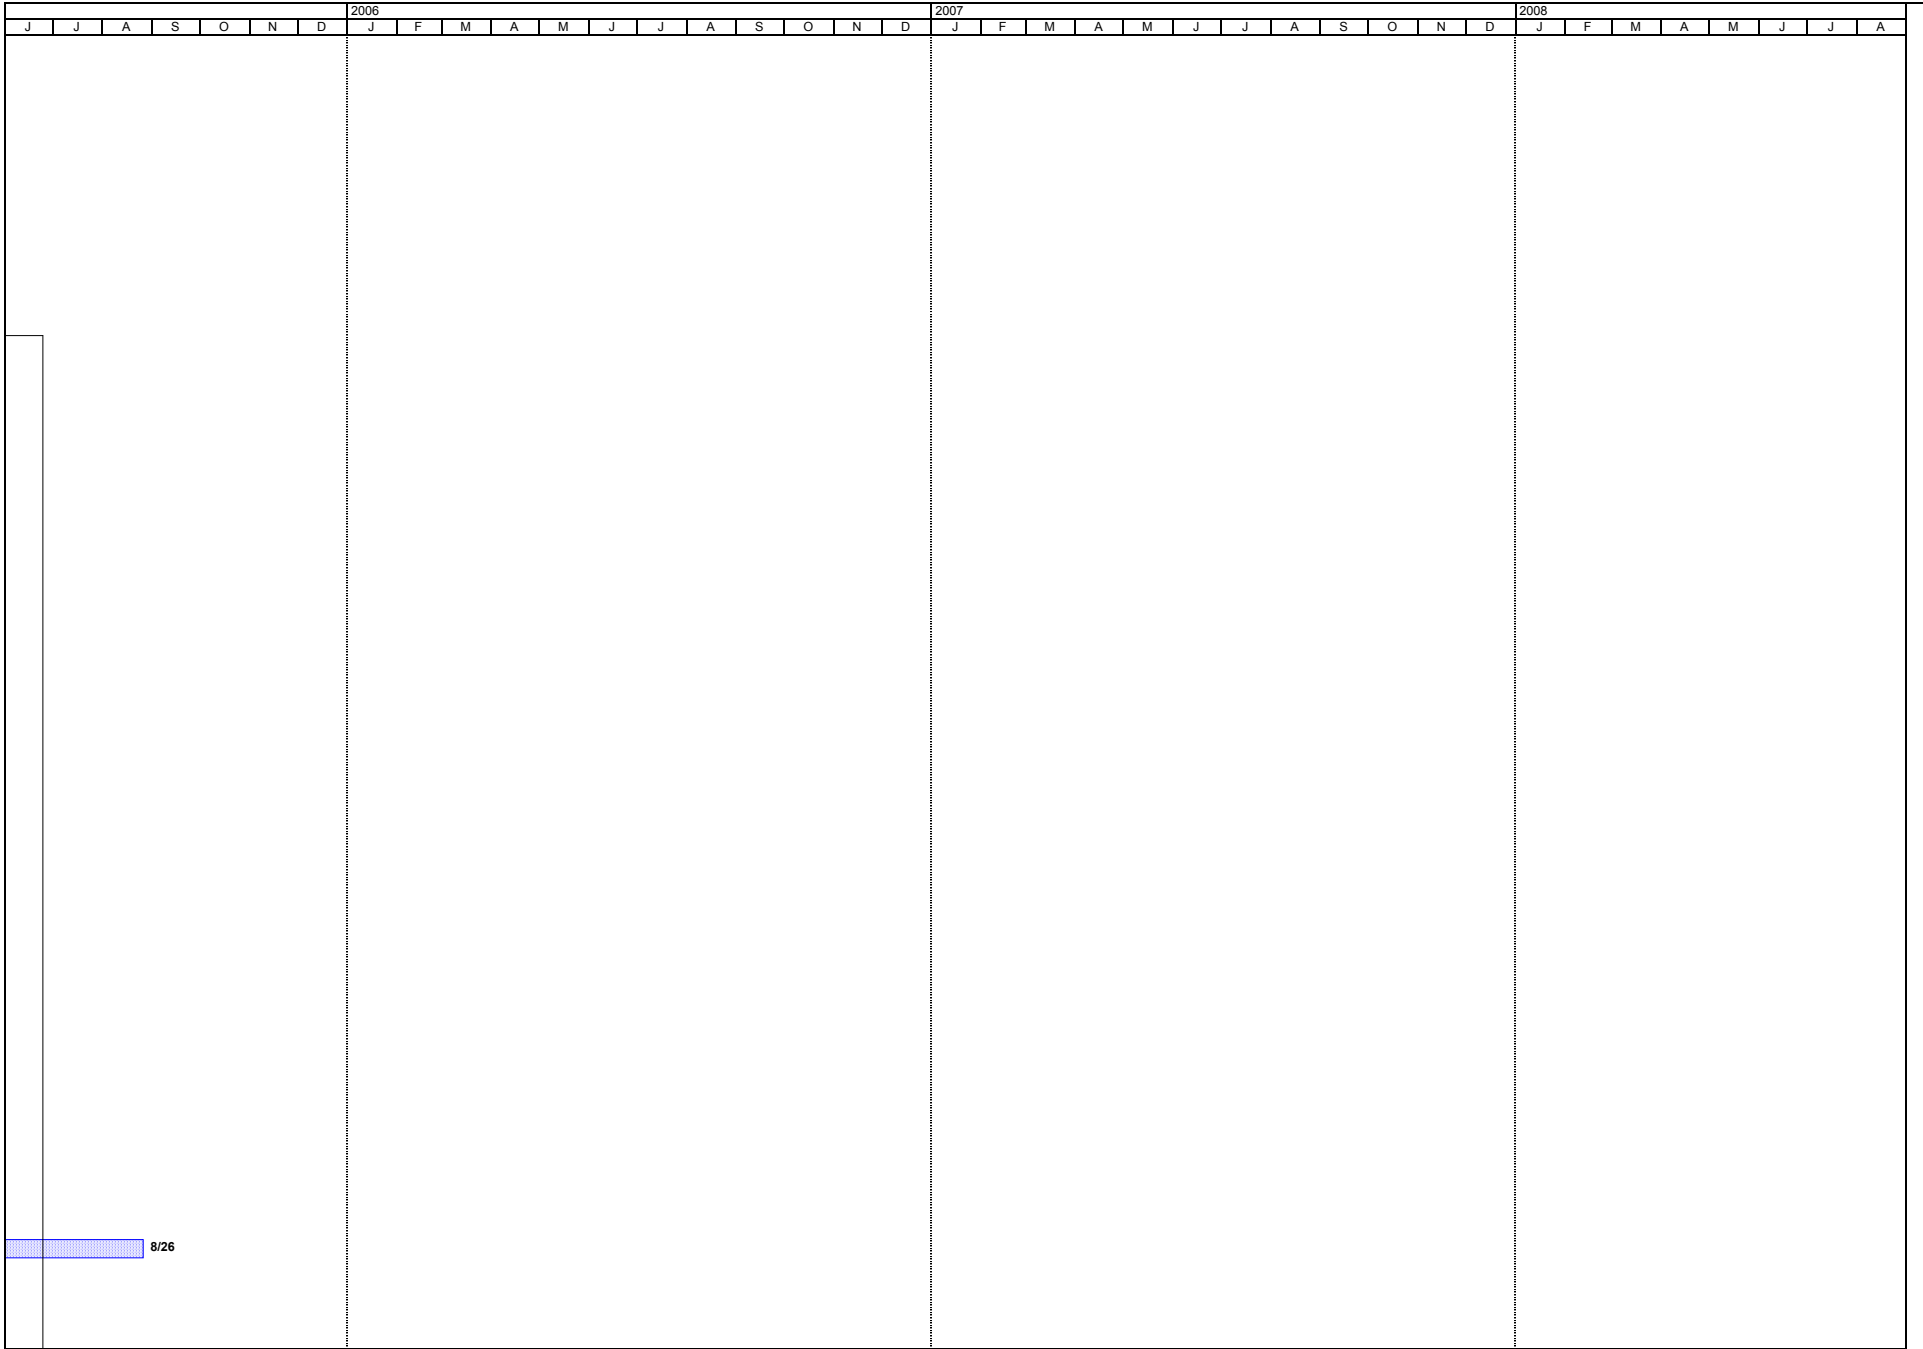

Project: Facilities_6_03 Date: 1/15/04	Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
	Progress		Summary		Rolled Up Milestone		Split		Project Summary			

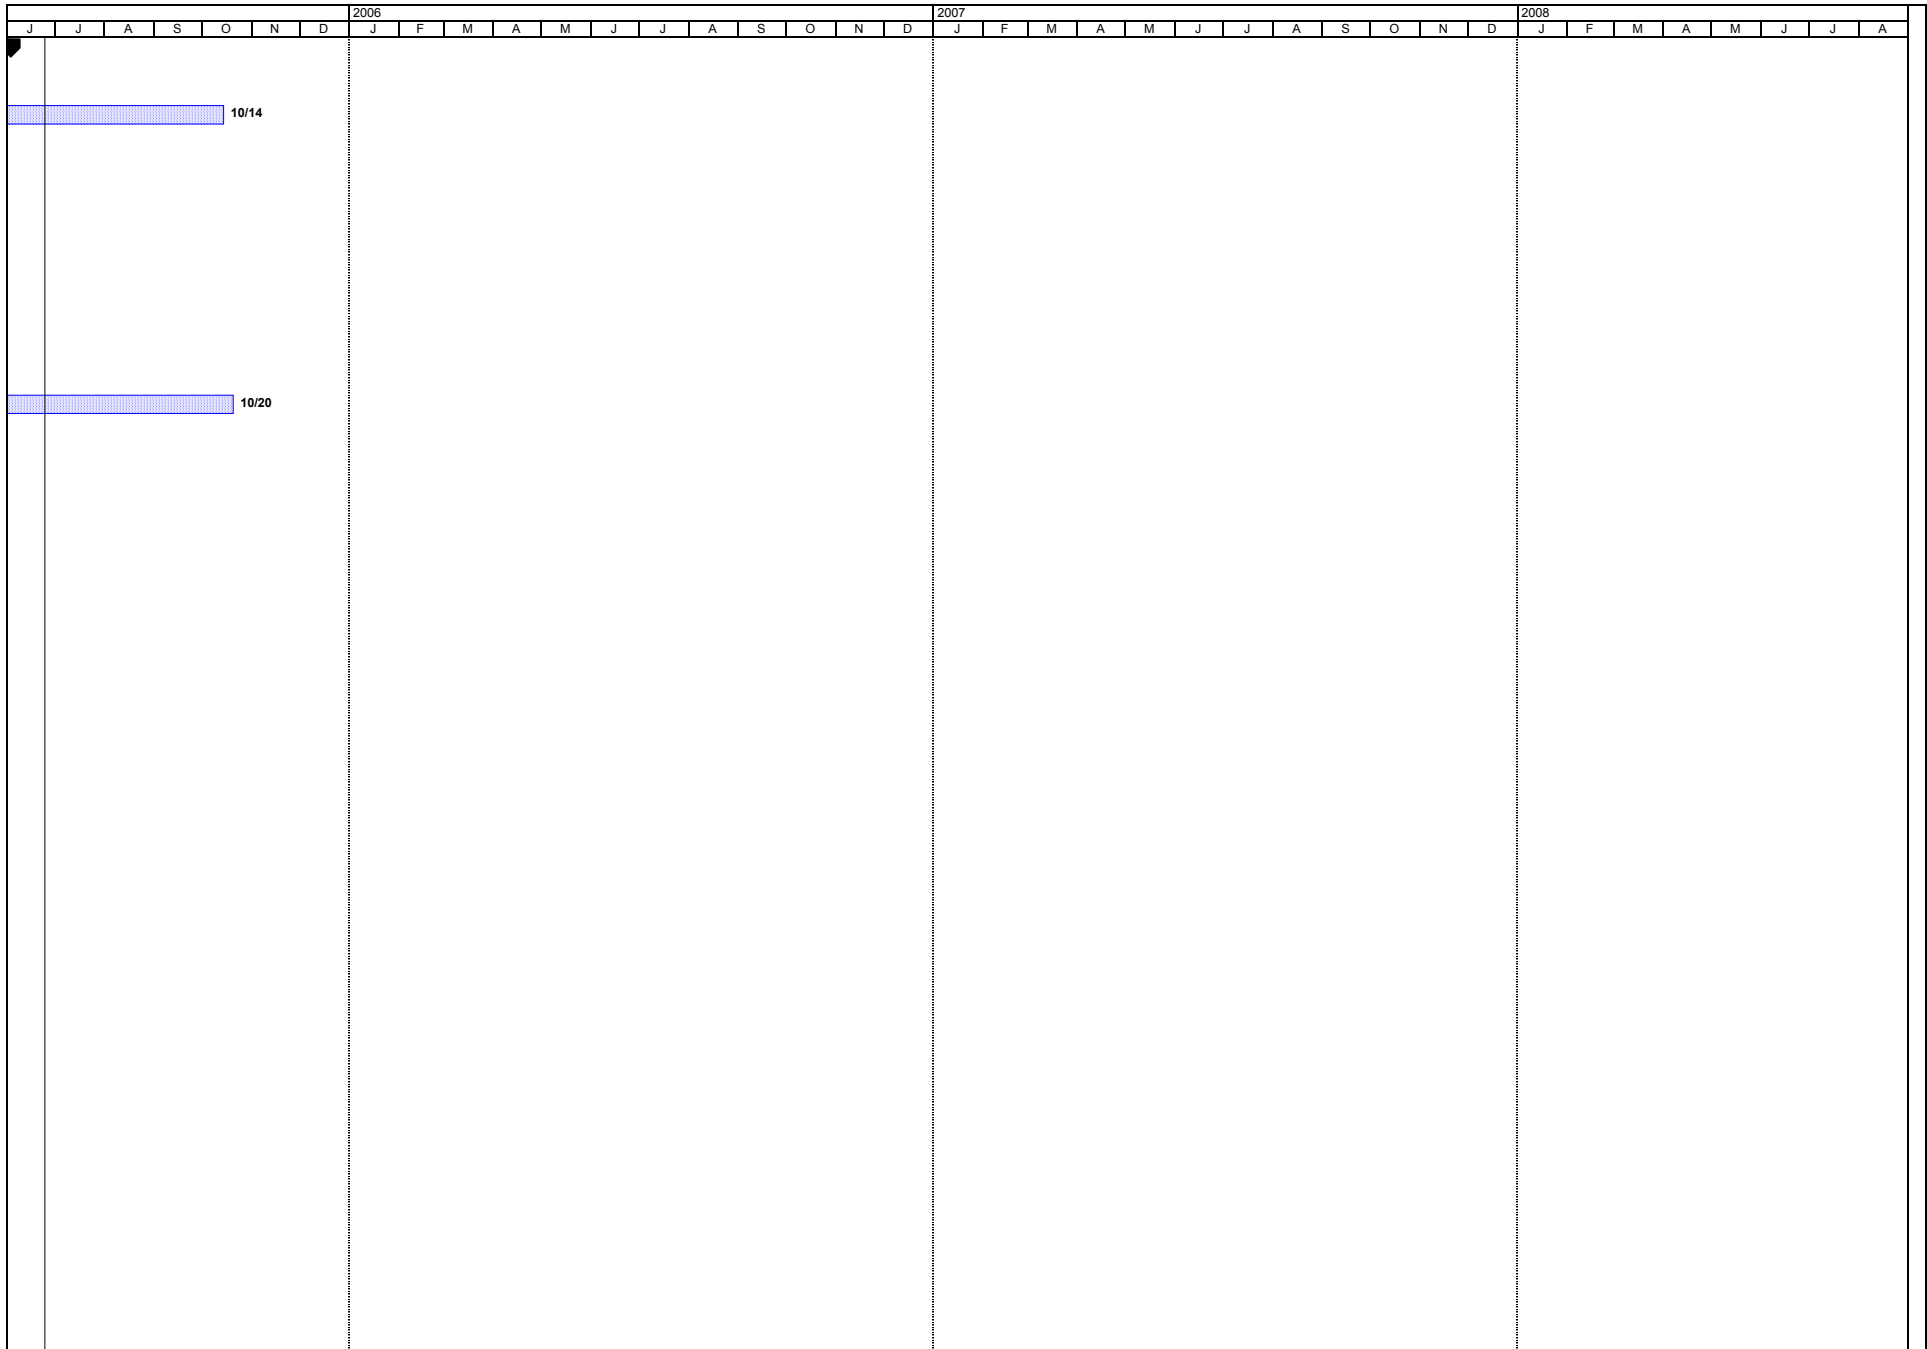


Project: Facilities_6_03 Date: 1/15/04	Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
	Progress		Summary		Rolled Up Milestone		Split		Project Summary			

2006												2007												2008														
J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A

Project: Facilities_6_03
Date: 1/15/04

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

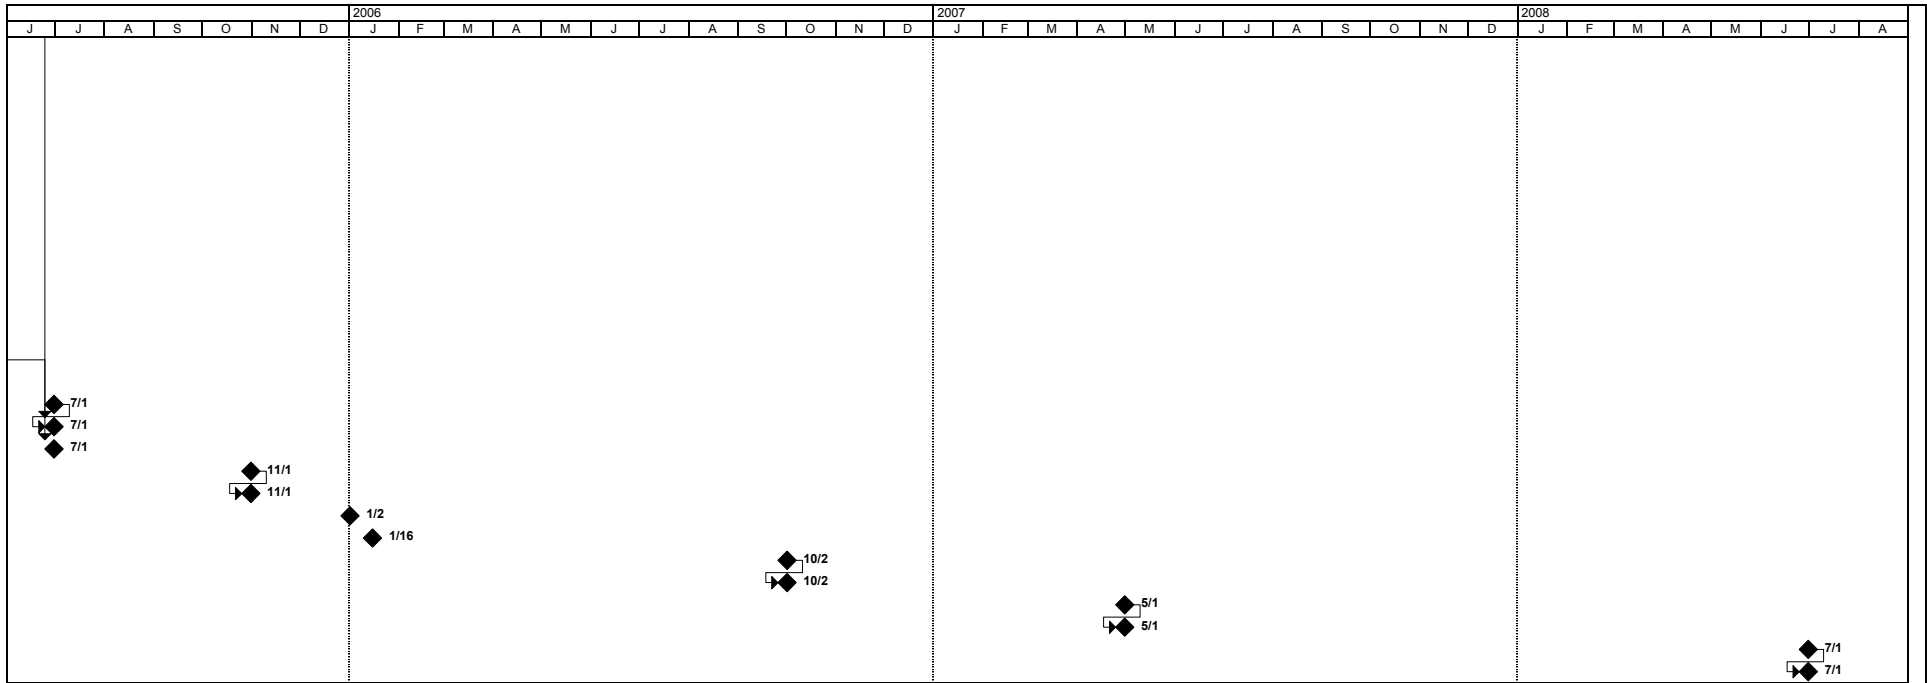

Project: Facilities_6_03
Date: 1/15/04

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			
