Svx_Sept03_v1.mpp Wed 9/10/03

ID	WBS	Task Name	Start	Finish	Duration
1	**1.1**	**Run 2b Silicon Project**	**Mon 7/2/01**	**Fri 5/19/06**	**1225 days**
7	**1.1.2**	**DAQ**	**Mon 7/2/01**	**Tue 5/9/06**	**1217 days**
274	**1.1.2.9**	**Fiber Transition Module Replacements**	**Fri 4/5/02**	**Tue 5/9/06**	**1028 days**
278	**1.1.2.9.2**	**FTM - 1st Preproduction**	**Fri 2/7/03**	**Mon 1/12/04**	**233 days**
279	***1.1.2.9.2.1***	***Explicit Slack: FTM design***	***Fri 3/7/03***	***Fri 3/7/03***	***0 days***
280	1.1.2.9.2.2	FTM: spec, design and layout	Fri 2/7/03	Fri 9/12/03	153 days
281	1.1.2.9.2.3	FTM Submission	Fri 9/12/03	Fri 9/12/03	0 days
282	1.1.2.9.2.4	FTM: procurement and assembly	Mon 9/15/03	Fri 11/7/03	40 days
283	1.1.2.9.2.5	FTM: test and evaluation	Mon 11/10/03	Mon 1/12/04	40 days
284	1.1.2.9.2.6	FTM available	Mon 1/12/04	Mon 1/12/04	0 days
285	**1.1.2.9.3**	**FTM preproduction**	**Wed 2/9/05**	**Fri 10/14/05**	**175 days**
286	***1.1.2.9.3.1***	***Explicit Slack: Preproduction and Production FTMs***	***Wed 2/9/05***	***Tue 3/1/05***	***3 wks***
287	1.1.2.9.3.2	Preproduction FTM: spec, design and layout	Wed 3/2/05	Tue 5/24/05	60 days
288	1.1.2.9.3.3	Preproduction FTM Submission	Tue 5/24/05	Tue 5/24/05	0 days
289	1.1.2.9.3.4	Preproduction FTM: procurement and assembly	Wed 5/25/05	Thu 7/21/05	40 days
290	1.1.2.9.3.5	Preproduction FTM: test and evaluation	Fri 7/22/05	Fri 10/14/05	60 days
291	1.1.2.9.3.6	Preproduction FTM available	Fri 9/2/05	Fri 9/2/05	0 days
292	**1.1.2.9.4**	**FTM Production**	**Mon 10/17/05**	**Tue 5/9/06**	**140 days**
293	1.1.2.9.4.1	Production FTM: spec, design and layout	Mon 10/17/05	Tue 12/13/05	40 days
294	1.1.2.9.4.2	Production go ahead on FTMs	Tue 12/13/05	Tue 12/13/05	0 days
295	1.1.2.9.4.3	Production FTM: procurement and assembly	Wed 12/14/05	Tue 2/14/06	40 days
296	1.1.2.9.4.4	Production FTM: test	Wed 2/15/06	Tue 5/9/06	60 days
297	1.1.2.9.4.5	Production FTM available	Tue 3/14/06	Tue 3/14/06	0 days
298	1.1.2.9.4.6	Production FTMs complete	Tue 5/9/06	Tue 5/9/06	0 days
299	**1.1.2.10**	**DAQ Testing & Readiness**	**Fri 12/6/02**	**Mon 1/10/05**	**523 days**
300	**1.1.2.10.1**	**DAQ: upper DAQ upgrade**	**Mon 5/19/03**	**Mon 1/10/05**	**412 days**
301	1.1.2.10.1.1	DAQ: SRC, FIB, VRB (FY 2003)	Mon 5/19/03	Wed 9/10/03	80 days
302	1.1.2.10.1.2	DAQ: SRC, FIB, VRB (FY 2004)	Wed 6/2/04	Tue 6/8/04	5 days
303	1.1.2.10.1.3	DAQ:SRC,FIB,VRB (FY 2005)	Tue 1/4/05	Mon 1/10/05	5 days
309	**1.1.2.10.3**	**DAQ Testing 2nd Round**	**Wed 9/10/03**	**Thu 12/4/03**	**60 days**
310	1.1.2.10.3.1	Testing of proto #2 DAQ chain	Wed 9/10/03	Tue 11/4/03	40 days
311	1.1.2.10.3.2	Go ahead for Preproduction	Tue 11/4/03	Tue 11/4/03	0 days
312	***1.1.2.10.3.3***	***Contingency: Go ahead for preproduction***	***Wed 11/5/03***	***Thu 12/4/03***	***4 wks***
313	1.1.2.10.3.4	Go ahead for Silicon Project DAQ Preproduction	Thu 12/4/03	Thu 12/4/03	0 days
314	**1.1.2.10.4**	**DAQ Testing Preproduction and Production**	**Wed 11/5/03**	**Fri 6/11/04**	**150 days**
315	1.1.2.10.4.1	Develop a new test DAQ system	Wed 11/5/03	Thu 3/18/04	90 days
316	1.1.2.10.4.2	Ready to test Preproduction DAQ chain	Thu 3/18/04	Thu 3/18/04	0 days
317	1.1.2.10.4.3	Testing of Preproduction DAQ chain	Fri 3/19/04	Thu 5/13/04	40 days
318	1.1.2.10.4.4	DAQ Production Go-Ahead	Thu 5/13/04	Thu 5/13/04	0 days
319	***1.1.2.10.4.5***	***Contingency: Go ahead for production***	***Fri 5/14/04***	***Fri 6/11/04***	***4 wks***
320	1.1.2.10.4.6	Go ahead for Silicon Project DAQ Production	Fri 6/11/04	Fri 6/11/04	0 days
392	**1.1.4**	**Cooling and Monitoring**	**Fri 10/18/02**	**Thu 4/13/06**	**873 days**
401	**1.1.4.3**	**Interlocks**	**Mon 6/27/05**	**Thu 4/13/06**	**200 days**
402	1.1.4.3.1	Upgrade existing system	Mon 6/27/05	Thu 4/13/06	200 days
409	**1.1.4.5**	**Radiation Monitoring**	**Fri 1/14/05**	**Wed 10/26/05**	**200 days**
410	1.1.4.5.1	Radiation monitors for inner(SVX and ISL) detector	Fri 1/14/05	Fri 3/11/05	40 days

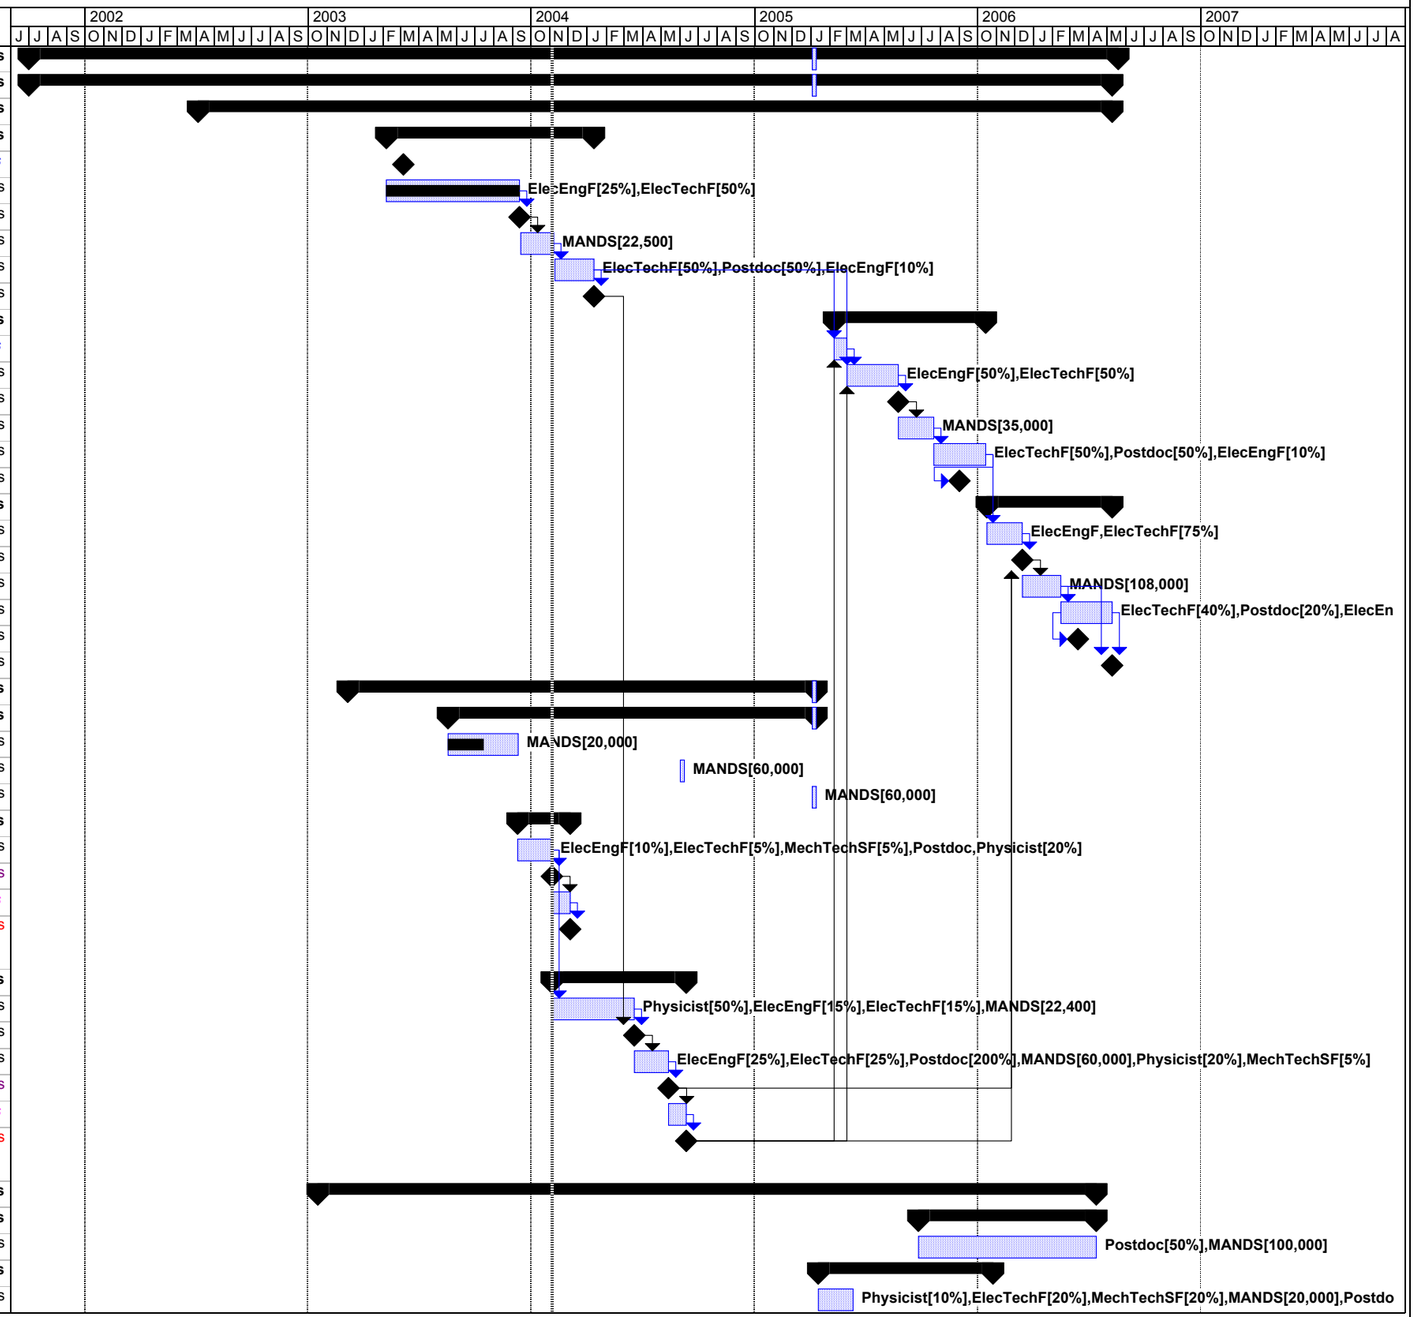

Project: CDF Run2
Date: Tue 11/4/03

Task Progress Milestone Summary Rolled Up Task Rolled Up Milestone Rolled Up Progress Split External Tasks Project Summary Group By Summary
