Status of Calibration Consumer

Youngdo Oh, Jaison Lee, Intae Yu

2/01/2002 TOF Meeting

Current Status

- QIE consumer

  Updated to 4.3.0 version

  -> executable is in ydoh's area

  Production calibration was taken on Jan/30

  -> Data looks fine.

  -> The executable will be moved to cdfdaq area

- TAC consumer

  Error handling in consumer

  -> Graphical framework done

  logical algorithm for error handling needs more work

Work is under transfer from Youngdo to Jaison

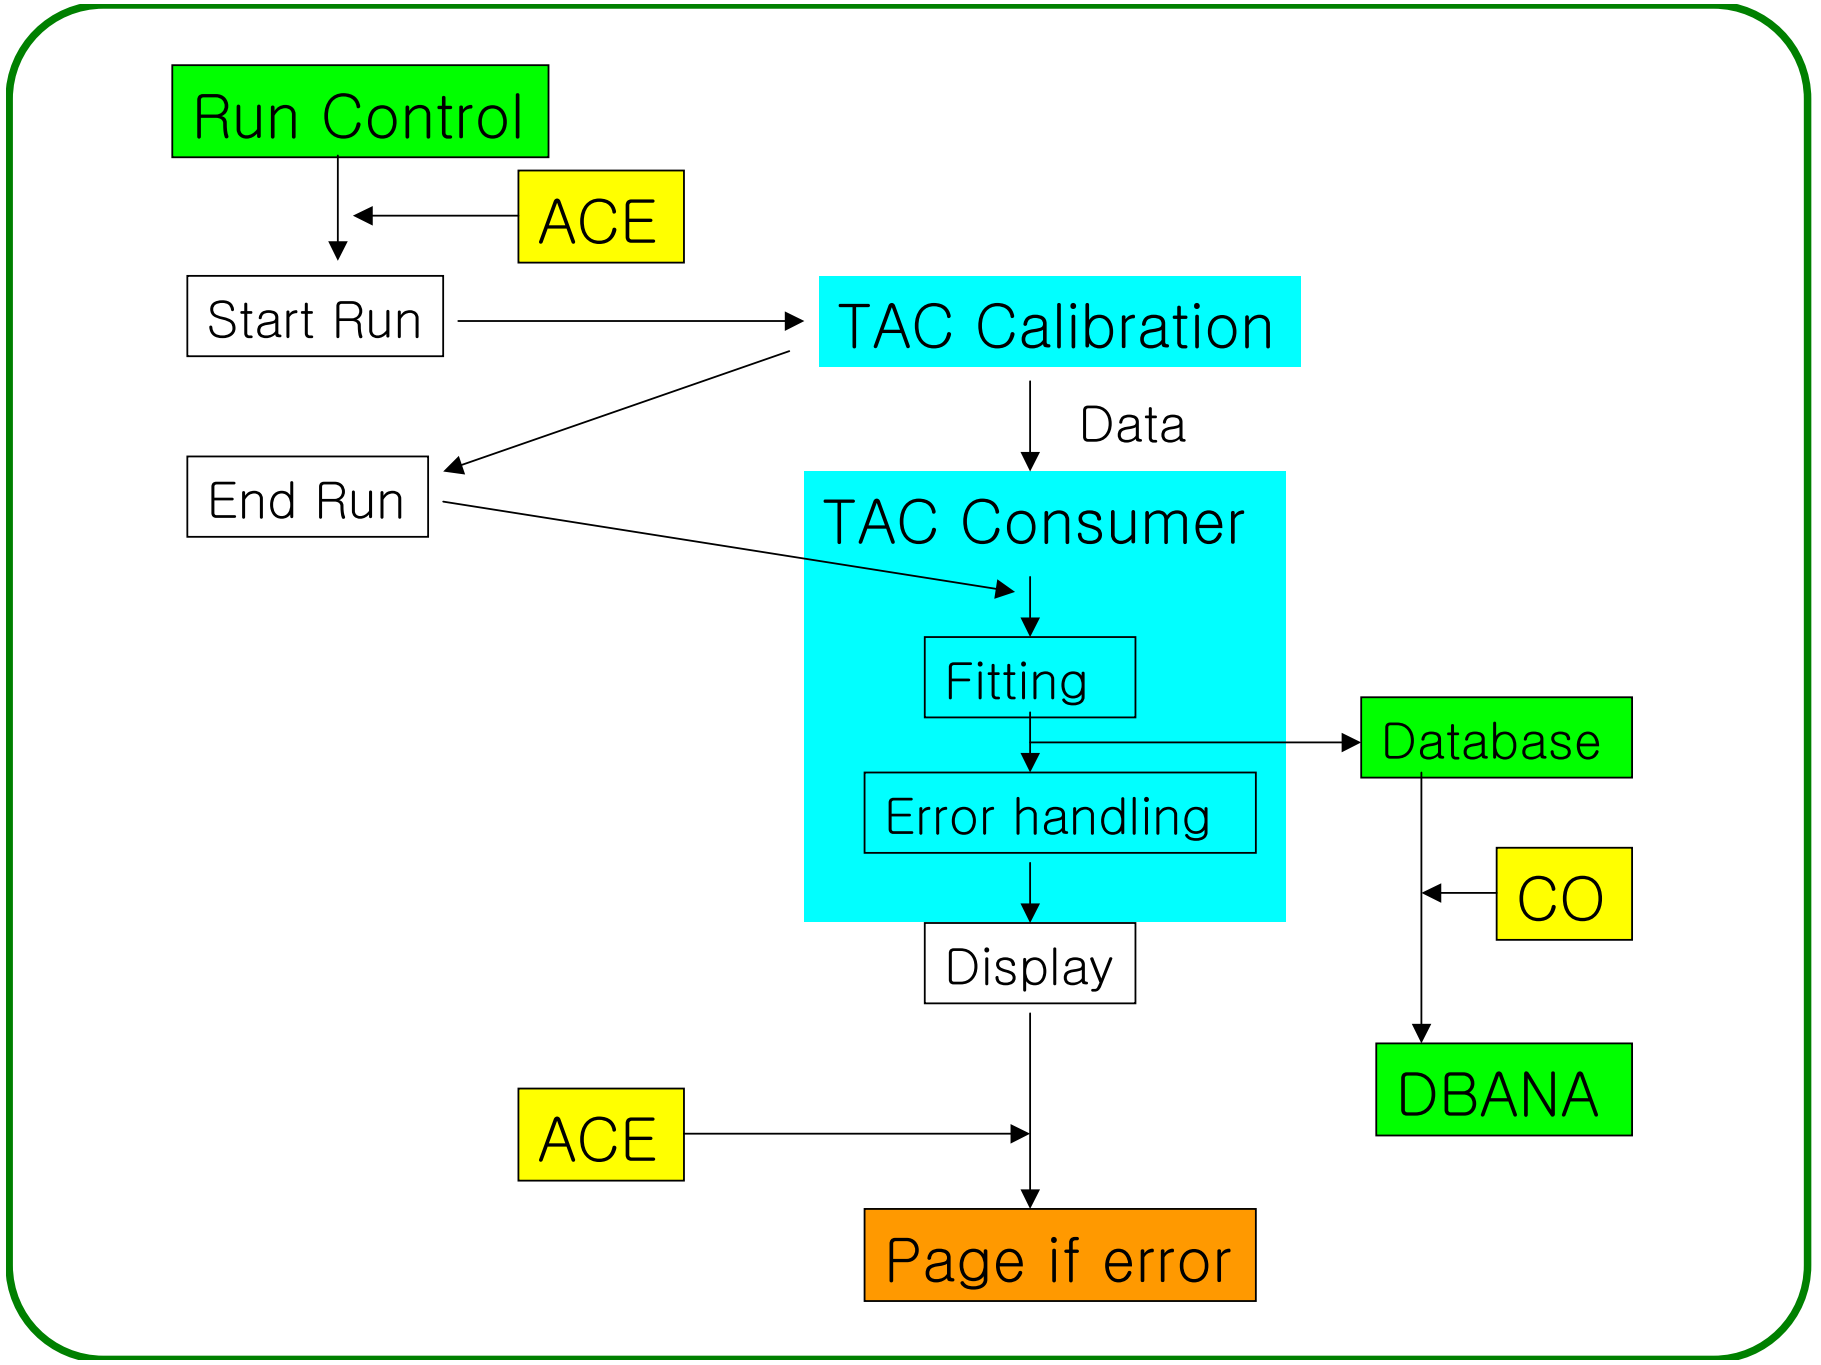
Run Control
ACE
Start Run
TAC Calibration
Data
End Run
TAC Consumer
Fitting
Database
Error handling
CO
Display
DBANA
ACE
Page if error

Plan

- Youngdo will focus on transferring work
- It will take ~ 3 weeks for Jaison to be trained fully with consumer and on-line work
- Version of consumer will be kept as the latest one of released cdfsoft.
- Youngdo will work on DBANA remotely and will transfer it to Jaison.

Time Schedule(Feb.1 – Feb.28)

- _TAC Consumer

  Feb.1 – Feb.15 Error handling (Y. Oh, J. Lee)

  Feb.16 – Feb.28 Debugging (J. Lee)

- DBANA

  Feb.8 – Feb.15 Frame Work (Y. Oh)

  Feb.16 – Feb.22 Add TOF module (Y. Oh, J. Lee, Gervasio)

  Feb.23 – Feb.28 Debugging (J. Lee, Gervasio)
