

NASA Contractor Financial Management Report:

Overview and Explanation of 533 Monthly and 533 Quarterly

Presented by: Acquisition Division



NASA Contractor Financial Management

Report

Overview

NF 533M Explanation

NF 533Q Explanation

Frequently Asked Questions, Dos and Don'ts

NASA Contractor Financial Management Report

Definition:

• The NASA Contractor Financial Management Report, comprised of NASA Forms 533 Monthly and 533 Quarterly (NF 533M and 533Q), is the basic financial medium for subcontractor reports of estimated and incurred costs

The NF 533M and 533Q:

- Provide essential data for projecting costs and hours to ensure that subcontractor performance is realistically planned and supported by dollar and labor resources
- Compare cost and time-phased baseline plan data
- Produce credible cost estimates
- Produce auditable financial reporting documents
- Should be as accurate as possible, so they may be used to facilitate informed, timely decisions and to project estimates at completion


What is the NASA Form 533 Monthly?

- A report which provides *monthly* data on actual and planned costs and labor hours, short-term cost projections, estimates at complete, subcontract values, and unfilled orders outstanding
- The NF 533M is required on Cost-type subcontracts greater than:
 - \$500,000 with a period of performance greater than 1 year or
 - \$1,000,000 regardless of period of performance (See slide 4)
- How do I submit the 533M?
 - Email it monthly to your Subcontract Manager (SM) and Payment Analyst (and others as may be designated by your SM)
 - Submit the 533M no later than 10 working days following the close of the subcontractor's monthly accounting period
- Reporting must begin no later than 30 days after first incurrence of cost

What is the NASA Form 533 Quarterly?

- A report which provides a *quarterly* update on time-phased cost and labor hour estimates required to complete the subcontract
- The NF 533Q is required on Cost-type subcontracts greater than:
 - \$1,000,000 with a period of performance greater than 1 year (See slide 4)
- How do I submit the 533Q?
 - Email it monthly to your Subcontract Manager (SM) and Payment Analyst (and others as may be designated by your SM)
 - Submit the 533Q no later than the 15th day of the month preceding the quarter being reported in columns 8a, 8b, and 8c (e.g., the report for the quarter beginning July is due not later than June 15)
- All subcontractors shall submit an initial report in the NF 533Q format within 30 working days after authorization to proceed has been granted
- NF 533M must also be submitted in months when an NF 533Q is submitted

NF 533M/Q Reporting Requirement

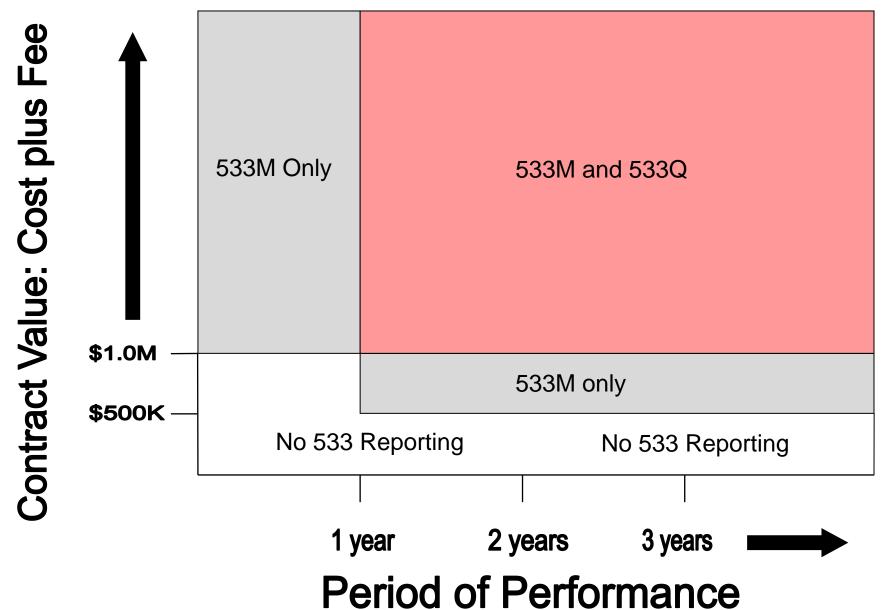



NASA Contractor Financial Management Report

Overview

NF 533M Explanation

NF 533Q Explanation

Frequently Asked Questions, Dos and Don'ts

Sample NF 533M

									PAGE	OF	PAGES
NASA	lational eronautics and ipace dministration		Contrac ment Re		ncial		Form Appro O.M.B. No.2	ved 2700-0003		Block 2	
TO:				FROM:					LCOST	5. CONTRACT VALUE	
	Block 1								5		
1. DESCRIPTION				b. CONTRACT NO. A	ND LATEȘT DEFINITIZ	2ED MODIFICATION N	0.		🖁 Blo	ocks 3 ·	- 5
OF CONTRACT	C. SCOPE OF WORK			d. AUTHORIZED CO	NTRACTOR REPRESE	NTATIVE (Signature)		DATE	LINVOICE AMTS. B	5. BILLING	PYTS. REC'D.
									\$	\$	
		DURING	7. COST INCURRE		O DATE		d Cost/Hours To Tail	COMPLETE		ATED FINAL HOURS	
6.F	REPORTING CATEGORY	ACTUAL	PLANNED	ACTUAL	PLANNED			BALANCE OF CONTRACT	CONTRACTOR	CONTRACT	10. UNFILLED ORDERS OUTSTANDING
		a	b.	c	d.	a.	b.	c	EŞTIMATE ā.	b.	00101740140
ļ											
1											
1	Diade C										10
1	Block 6		Bloc	СК /			Block 8	5	BI00	cks 9 -	10
										1	
										1	
										1	
]											
										<u> </u>	
<u> </u>										+	
<u> </u>		-									
	Deselles Dies Idealitestics (D.								1		
	Baseline Plan Identification (Co				Di	ted					CS 10PUBL00417
NASA FORM 533	AUG 96 PREVIOUS EDITION	SARE OBSOLETE.									05 10-00000417
	Block 11										

NF 533M Content: Blocks I-2



NF 533M form heading shall contain the following:

Block	То	Enter the full name and address of JPL
Block	From	Enter the subcontractor's name and mailing address if applicable, the division performing the subcontract
Block 1.a	Туре	The subcontract type, Cost-Plus-Fixed-Fee, Cost-Plus- Incentive-Fee, etc
Block 1.b	Contract No.	The subcontract number & latest definitized modification number
Block 1.c	Scope Of Work	Brief description of the subcontract effort; Identify the service, project, or system and the quantity being procured
Block 1.d	Authorized Subcontrac- tor Rep.	The authorized subcontractor representative shall <i>sign</i> and date the summary page to reflect approval; Electronic signatures are encouraged
Block 2	Reporting For Months Ending-	Enter the ending date of the subcontractor's accounting month and the number of working days for that accounting month

- 8 -

NF 533M Content: Blocks 3-5

		F		-		5	cia 1.1
20.000		-		-	-		-
	-		1	- 1		w	Ψ.
			-				
		-	-				
-					-		

NF 533M form heading shall contain the following:

Block 3.a	Contract Value Cost	The total cost (a) and fee (b) of all definitized work to be performed under the subcontract. Include dollar amounts
Block 3.b	Contract Value Fee	through latest definitized modification as noted in block 1b.
Block 4	Fund Limitation	Enter the total funds authorized by JPL thru the reporting period and latest corresponding subcontract modification number
Block 5.a	Invoice Amounts Billed	Enter the total dollar amount of invoices billed against the subcontract and latest invoice number
Block 5.b	Total Payments Received	Enter the total dollar amount of payments received for the subcontract

NF 533M Reporting Categories: Block 6



• JPL requires costs to be identified by:

- 10 -

- Elements of cost are uses for which resources are expended in performance of the subcontract
 - This type of information provides insight for JPL concerning the way resources are expended and aids in comparing actual to negotiated cost rates
 - Direct labor, materials, subcontracts, other direct costs, indirect costs, G&A, and fees
- In addition, JPL may requires costs to be identified by:
 - **WBS** is a family tree subdivision of effort required to achieve an objective
 - May be hardware, product, service, or process oriented
 - Developed by starting with end objective & subdividing it into manageable components in terms of size, duration, and responsibility (e.g., systems, subsystems, components, tasks, subtasks, and work packages) to include all steps necessary to achieve objective

-or-

- **Organizational/Functional** data provide information on groups of activities which have a common purpose; these types of data may be required in order to:
 - Track costs by the subcontractors' internal organizations
 - Perform analysis-relating organizational/functional costs to end items
 - E.g. Engineering/Design, Manufacturing/Fabrication, Assembly, Test, Mission Ops, etc
- When subcontract includes only one subdivision of work, reporting by elements of cost will generally be sufficient. Otherwise, the JPL Subcontract Manager will determine level of reporting

Elements of Cost Reporting Category



- Elements of cost are typically classified as direct or indirect (burden). It may be necessary to determine the recurring and nonrecurring nature of cost
 - Direct costs can be specifically identified with a particular objective, such as a system, task, or function. Direct costs are classified as follows:
 - Labor
 - Materials
 - Subcontracts
 - Other Direct Costs
 - Indirect costs (burden) are, because of their incurrence for joint objectives, not identifiable to a specific objective. Indirect costs are classified as follows:
 - Overhead
 - General and Administrative (G&A)
- Reporting indirect costs in the same detail as direct costs may be complex, especially where there are interrelated overhead pool structures. JPL requires a breakdown of the various types of burdens, e.g., engineering overhead, manufacturing overhead, material handling, and G&A, in order to provide visibility and track actual and provisional rates

NF 533M Content: Block 7



NF 533M form shall contain the following:

Block 7	Cost Incurred/ Hours Worked	Cost and hour data will be reported in the categories specified in the subcontract
Block 7.a	Actual During Month	Enter the total actual cost incurred/hours worked for the accounting month being reported (block 2)
Block 7.b & d	Planned	Enter planned cost for the month being reported in column 7b and cumulative to date in column 7d. <i>The</i> <i>planned cost is obtained from the time-phased</i> <i>baseline plan,</i> which includes the original subcontract value plus authorized changes. Identify the baseline plan used by date/revision number in block 11.
Block 7.c	Actual Cum to Date	Enter the cumulative actual cost incurred/hours worked. Actual costs reported will include costs incurred in performing currently authorized work, i.e., all work directed, whether or not negotiated. Costs incurred <i>will be reported irrespective of whether they exceed</i> <i>the "Fund Limitation"</i> (block 4).

NF 533M Content: Block 8

-		_	-		_	_		in		
20			-			-	-	-	29	
	1			-	-	1	w	-	÷	ŀ
						Black				Ē
					-	-				ł
								-		ŧ
									-	Ē
and the second second	-		-		_		-	_		÷

NF 533M form shall contain the following:

Block 8	Estimated Cost/Hours to Complete	Enter the current <i>short-term estimates</i> for performing authorized work included in the most recently executed subcontract modification, plus additional authorized work (directions to proceed) for which execution of modifications is pending. The <i>estimates will be for</i> <i>planning purposes only</i> and will not be binding on either the subcontractor or JPL. <i>Data entered will not be</i> <i>simply a restatement of negotiated baseline values.</i>
Block 8.a		Show the most current estimate for the next month
Block 8.b		Show the most current estimate for the subsequent month thereafter
Block 8.c	Balance of Contract	Enter the cost/hour data for the balance of the subcontract not including columns 8a and 8b.

NF 533M Content: Blocks 9-11

	Ē			5m					
	- 17	1		÷.	7	-	4	÷.	1
							Bux	84 F	10
									Ē
	-				-				-

NF 533M form shall contain the following:

Block 9	Estimated Final Cost/Hours:	This long-term estimate enables JPL to compare the subcontract value to the current estimate at completion and identify potential over or underruns
Block 9.a	Contractor Estimate	Enter the total estimated cost/hours at completion of the subcontracted effort by reporting categories (should equal the sum of columns 7c, 8a, 8b and 8c)
Block 9.b	Contract Value	Enter the distribution of the subcontract value to the reporting categories. The total of this column shall agree with block 3. Significant differences between columns 9a and 9b shall be explained in block 11.
Block 10	Unfilled Orders Outstanding	The difference between cumulative costs incurred to date and amounts obligated to suppliers, to include open purchase orders, in which <i>materials have not been received nor services rendered</i>
Block 11	Narrative Remarks	Explain items materially affecting historical/projected cost or performance for each monthly report

NF 533M Content: Long Term Cost Estimates

- Long-term cost estimates, which include all data entered in column 9a on NF 533M and NF 533Q reports, shall be based on the most current and reliable information available
 - Contractor Estimate shall present the subcontractor's estimated costs at completion
 - They are used for planning purposes only and are not binding to the subcontractor or JPL
 - Data entered will not be simply a restatement of negotiated baseline values
 - Subcontractors shall provide the most accurate long-term estimates that consider the cost, schedule, or technical outcome of the subcontract
 - Long-term estimates shall be reported without regard to negotiated subcontract cost block (3a &b)
 - Subcontractors shall include potential overruns or underruns when recognized



NASA Contractor Financial Management Report

Overview

NF 533M Explanation

NF 533Q Explanation

Frequently Asked Questions, Dos and Don'ts

Sample NF 533Q

														PAGE		F	PAGES
National Aeronautics and Space Administration		Quart	erly Co	ontract	tor Fin	ancial	Manag	gemen	t Repo	ort	Form I O.M.B	Approve No. 270	d 0-0003	2. REPOR	Blo	ck 2]
TO:						FROM:								LCOST	3.CONTRA	b. FEE	
Block 1														s			_
	a. TYPE						b. CONTRACT	T NO. AND LAT	EST DEFINIT	IZED MODIFIC	ATION NO.			BI	ocks	s 3 -	5
1. DESCRIPTION OF CONTRACT	c. SCOPE OF	FWORK					d ALITHORIZ	ED CONTRAC	TOR REPRES	ENTATI//F /S/n	naturel	DATE		s	5. BIL		
CONTRACT														LINVOICE A	MTS. BILLED		78. REC'D.
		COST INCUR			_		8.ESTIMA	TED COST/H	OURS TO C	OMPLETE	_			9. ESTIMA COST/			
6. REPORTING CATEGORY	CUMU- LATIVE			MONTH	MONTH	MONTH	QUARTER	QUARTER	QUARTER	BALANCE OF	NEXT	BALANCE OF CONTRACT	TOTAL TO COMPLETE	CONTRACTOR	CONTRACT	10. ESTI- MATED COM-	11. UNFILLED ORDERS
	CUMU- LATIVE ACTUAL THROUGH PRIOR MONTH	CUR- RENT MONTH ESTI- MATE	CUMU- LATIVE ESTI- MATE TO DATE							PY-	PY-	CONTRACT	COMPLETE	EDIMATE	VALUE	PLETION DATE	OUT- STANDING
}	*	b.	e	8.	ь.	¢.	d.	e.	L	g.	h	L	1	8.	b.		
	-		<u> </u>														
			-						•							<u>^</u>	
Block 6	HВ	lock	1					Block	8					- BIC	ocks	9 -	11
1																	
			<u> </u>														
NASA FORM 533Q AUG 95 PREVI	OUS EDITION	S ARE OBSC	LETE.									_			_	RCS 1Ø	PUBLØØ417
Block 12																	
DIUCK IZ																	

NF 533Q Content: Blocks I-2



NF 533Q form heading shall contain the following:

Block	То	Enter the full name and address of JPL
Block	From	Enter the subcontractor's name and mailing address if applicable, the division performing the subcontract
Block 1.a	Туре	The subcontract type, Cost-Plus-Fixed-Fee, Cost-Plus- Incentive-Fee, etc
Block 1.b	Contract No.	The subcontract number & latest definitized modification number
Block 1.c	Scope Of Work	Brief description of the subcontract effort; Identify the service, project, or system and the quantity being procured
Block 1.d	Authorized Subcontrac- tor Rep.	The authorized subcontractor representative shall <i>sign</i> and date the summary page to reflect approval; Electronic signatures are encouraged
Block 2	Reporting For Months Ending-	Enter the ending date of the subcontractor's accounting month and the number of working days for that accounting month

<u>- 18 -</u>

NF 533Q Content: Blocks 3-5

	-		_	_		Г.							_	ī,	lich	3.
30	-	-			_			-		-	-	1		E	- 27	
	₽	ŧ	R	-	-	1	17	-	-	F	7	-	-	10	÷.	볋
						E	E									
	E	E	E			E	E	E	E			E		-		
	E		E			E	E		E			E				
	E		E			E	E			E		E				
	-															_

NF 533Q form heading shall contain the following:

Block 3.a	Contract Value Cost	The total cost (a) and fee (b) of all definitized work to be performed under the subcontract. Include dollar amounts						
Block 3.b	Contract Value Fee	hrough latest definitized modification as noted in block 1b.						
Block 4	Fund Limitation	Enter the total funds authorized by JPL thru the reporting period and latest corresponding subcontract modification number						
Block 5.a	Invoice Amounts Billed	Enter the total dollar amount of invoices billed against the subcontract and latest invoice number						
Block 5.b	Total Payments Received	Enter the total dollar amount of payments received for the subcontract						

NF 533Q Reporting Categories: Block 6



- JPL requires costs to be identified by:
 - Elements of cost are uses for which resources are expended in performance of the subcontract
 - This type of information provides insight for JPL concerning the way resources are expended and aids in comparing actual to negotiated cost rates
 - Direct labor, materials, subcontracts, other direct costs, indirect costs, G&A, and fees
- In addition, JPL may requires costs to be identified by:
 - WBS is a family tree subdivision of effort required to achieve an objective
 - May be hardware, product, service, or process oriented
 - Developed by starting with end objective & subdividing it into manageable components in terms of size, duration, and responsibility (e.g., systems, subsystems, components, tasks, subtasks, and work packages) to include all steps necessary to achieve objective

-or-

- Organizational/Functional data provide information on groups of activities which have a common purpose; these types of data may be required in order to:
 - Track costs by the subcontractors' internal organizations
 - Perform analysis-relating organizational/functional costs to end items
 - E.g. Engineering/Design, Manufacturing/Fabrication, Assembly, Test, Mission Ops, etc
- <u>- 20 -</u> When subcontract includes only one subdivision of work, reporting by elements of cost will generally be sufficient. Otherwise, the JPL Subcontract Manager will determine level of reporting

Elements of Cost Reporting Category



- Elements of cost are typically classified as direct or indirect (burden). It may be necessary to determine the recurring and nonrecurring nature of cost
 - Direct costs can be specifically identified with a particular objective, such as a system, task, or function. Direct costs are classified as follows:
 - Labor
 - Materials
 - Subcontracts
 - Other Direct Costs
 - Indirect costs (burden) are, because of their incurrence for joint objectives, not identifiable to a specific objective. Indirect costs are classified as follows:
 - Overhead
 - General and Administrative (G&A)
- Reporting indirect costs in the same detail as direct costs may be complex, especially where there are interrelated overhead pool structures. JPL requires a breakdown of the various types of burdens, e.g., engineering overhead, manufacturing overhead, material handling, and G&A, in order to provide visibility and track actual and provisional rates

NF 533Q Content: Block 7

-		TAX IS INCOME.	-
301		 	
	# # R		~~~~
	Euch 7		
	and the second		
_			

NF 533Q form shall contain the following:

Block 7	Cost Incurred/ Hours Worked	Cost and hour data will be reported in the categories specified in the subcontract
Block 7.a	Cum. Actual Thru Prior Month	Enter the cumulative actual cost incurred/hours worked through the prior month
Block 7.b	Current Month Estimate	Enter an estimate for the month in which the report is due (see submission date)
Block 7.c	Cum. Estimate To Date	Enter the sum of columns 7a and b

NF 533Q Content: Block 8

			_	_	_	-					_	5	_	-
30						-						-		
	¢	ŧ	R	1 -	-	0	-	1	-	-			¥.	響

NF 533Q form shall contain the following:

Block 8 Block 8.a Thru 8.h	Estimated Cost/Hours to Complete	Enter the appropriate month, quarter and fiscal year designations in the column headings. Enter the current estimates for performing authorized work, included in the most recently executed subcontract modification, plus additional authorized work. The <i>estimates will be for planning purposes only</i> and will not be binding on either the subcontractor or JPL. <i>Data</i> <i>entered will not be simply a restatement of</i> <i>negotiated baseline values.</i>
Block 8.i	Balance of Contract	Enter the cost/hour data for the balance of the subcontract not including columns 8a thru 8h.
Block 8.j	Total To Complete	The sum of columns 8a through 8i

NF 533Q Content: Blocks 9-12



NF 533Q form shall contain the following:

Block 9	Estimated Final Cost/Hours:	This long-term estimate enables JPL to compare the subcontract value to the current estimate at completion and identify potential over or underruns
Block 9.a	Contractor Estimate	Enter total estimated cost/hours at completion of the subcontracted effort by reporting categories (7c+8j)
Block 9.b	Contract Value	Enter the distribution of the subcontract value to the reporting categories. The total of this column shall agree with block 3. Significant differences between columns 9a and 9b shall be explained in block 12.
Block 10	Est. Comple- tion Date	Enter completion date for each subdivision of work. <i>Entry doesn't serve as notice to JPL of late delivery</i>
Block 11	Unfilled Orders Outstanding	The difference between cumulative costs incurred to date and amounts obligated to suppliers, to include open purchase orders, in which <i>materials have not been received nor services rendered</i>
Block 12	Narrative Remarks	Explain items materially affecting historical/projected cost or performance for each monthly report

- 24 -

NF 533Q Content: Long Term Cost Estimates

- Long-term cost estimates, which include all data entered in column 9a on NF 533M and NF 533Q reports, shall be based on the most current and reliable information available
 - Contractor Estimate shall present the subcontractor's estimated costs at completion
 - They are used for planning purposes only and are not binding to the subcontractor or JPL
 - Data entered will not be simply a restatement of negotiated baseline values
 - Subcontractors shall provide the most accurate long-term estimates that consider the cost, schedule, or technical outcome of the subcontract
 - Long-term estimates shall be reported without regard to negotiated subcontract cost block (3a &b)
 - Subcontractors shall include potential overruns or underruns when recognized



NASA Contractor Financial Management Report

Overview

NF 533M Explanation

NF 533Q Explanation

Frequently Asked Questions, Dos and Don'ts

Frequently Asked Questions

Q: Why must I submit financial management reports to JPL?

A: A Cost-reimbursable subcontract removes almost all cost risk from the subcontractor and places this risk on JPL. The NF 533M and 533Q provides JPL with the information to manage this cost risk. Without transparency, JPL would consistently develop unrealistic cost and schedule estimates, which in part, contribute to cost growth and schedule increases in many of its projects. Each NF 533M and 533Q will continue to strengthen JPL's ability to manage its highly complex projects.

Q: Why must I submit 2 separate forms, NF 533M and NF533Q?

A: Each form has a different time-frame focus: the **NF 533M** compares actual cost-to-date to the original cost plan, and provides a new estimate of work for the next two months. JPL requires this information every month. The **NF 533Q** prepares new time-phased cost and labor hour estimates required to complete the subcontract according to the most recent schedule update. JPL requires this information before the beginning of every quarter.

Q: What happens if I don't comply with the reporting requirements?

A: Non-compliance can result in grade and award fee reduction. In the event a subcontractor fails to submit required NF 533 reports on a timely basis or in an accurate manner, JPL is not required to make payment on cost and fee vouchers by contractual due dates and may withhold payment until compliance is clearly demonstrated.

Q: Can I just put the values from my Baseline Plan into the corresponding columns 8 of the NF 533M and NF 533Q?

A: JPL knows the monthly planned values because they are indicated in the previously submitted Baseline Cost Estimate. In Column 8, please give your latest forecast or estimate for the time period in question.

Top Dos and Don'ts

NF 533M

- Make sure "Planned" dollars (Col. 7b & d) reflect the latest Baseline Cost Estimate by month submitted to JPL, and identify that plan in block 11
- Get Column 8a right: Consider the Actual Cost you have incurred through the date you submit the report, and whether the material deliveries and subcontractor performance that you have based your estimated cost on will actually materialize by the end of the month. JPL will compare the cost estimate in Column 8a with the Actual Cost you report in Column 7a on the following month's 533M report to assess your ability to provide reliable near-term cost estimates.
- Accurately report Unfilled Orders Outstanding (Col. 10)
- Ensure the consistent application of what constitutes an actual cost. Always restate that definition in block 11

NF 533Q

- 28 -

- Include all work authorized by JPL, not just definitized work in Estimated Cost/Hours to Complete (Col. 8)
- Reflect government fiscal-quarter calendar and ensure the NF 533Q is submitted in the month *prior* to the Quarter in Col. 8a, b, and c.
- Be able to justify the phasing in Columns 8
- Be sure columns 8 and 9a reflect subcontractor's latest forward-pricing rates
- Make sure Contractor Estimate (Col. 9a) accurately reflects costs and labor hours required to finish the job. Do not consider how JPL will react to the news
- Explain why Col 9a differs from 9b



Still have questions?

Contact your Subcontract Manager

NPR 9501.2D

 Click the link for NASA Procedural Requirements (NPR) 9501.2D: NASA Contractor Financial Management Reporting

http://nodis3.gsfc.nasa.gov/displayDir.cfm?Internal_ID=N_P R_9501_002D_&page_name=Chp1
